STATE OF NORTH DAKOTA

BOARD OF WATER WELL CONTRACTORS

900 E. BOULEVARD • BISMARCK, NORTH DAKOTA 58501

WELL DRILLER'S REPORT

State law requires that this report be filed with the State Board of Water Well Contractors within 30 days after completion or abandonment of the well.

1. WELL OWNER

Name Sig Mock

Address Kintyre, N. Dak.

2. WELL LOCATION

Sketch map location must agree with written location.

NORTH

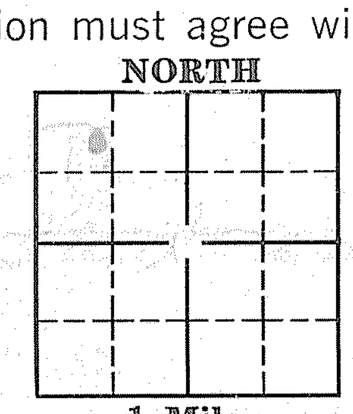

1 Mile

County EMMONS

SE ¼ NW ¼ NW ¼ Sec. 33 Twp. 136 N. Rg. 74 W.

3. PROPOSED USE

☐ Domestic ☐ Irrigation ☐ Industrial

☒ Stock ☐ Municipal ☐ Test Hole

4. METHOD DRILLED

☐ Cable ☐ Reverse Rotary ☐ Bored

☒ Forward Rotary ☐ Jetted ☐ Other

If other, specify

5. WATER QUALITY

Was a water sample collected for chemical analysis?

☐ Yes ☒ No

If so, to what laboratory was it sent

6. WELL CONSTRUCTION

Diameter of hole 4 inches. Depth 223 feet.

Casing: ☐ Steel ☒ Plastic ☐ Concrete

☐ Threaded ☐ Welded ☐ Other

If other, specify

Pipe Weight:	Diameter:	From:	To:
Sch 40 lb/ft.	4 inches	0 feet	140 feet
lb/ft.	inches	feet	feet
lb/ft.	inches	feet	feet
lb/ft.	inches	feet	feet

Was perforated pipe used? ☐ Yes ☒ No

Length of pipe perforated feet

Was casing left open end? ☒ Yes ☐ No

Was a well screened installed? ☐ Yes ☒ No

Material Diameter inches
(stainless steel, bronze, etc.)

Slot size set from feet to feet

Slot size set from feet to feet

Slot size set from feet to feet

Slot size set from feet to feet

Was a packer or seal used? ☐ Yes ☒ No

If so, what material

Type of well: Straight screen ☒ Gravel packed ☐

Was the well grouted? Yes ☐ No ☒

To what depth? feet

Material used in grouting

Well head completion: Pitless adapter

12" above grade X Other

If other, specify

Was well disinfected upon completion? ☒ Yes ☐ No

7. WATER LEVEL

Static water level 6 feet below land surface

If flowing: closed-in pressure psi

GPM flow through inch pipe

Controlled by: ☐ Valve ☐ Reducers ☐ Other

If other, specify

8. WELL TEST DATA

☒ Pump ☐ Bailer ☐ Other

Pumping level below land surface:

32 ft. after 6 hrs. pumping 5 gpm

ft. after hrs. pumping gpm

ft. after hrs. pumping gpm

9. WELL LOG

Formation	Depth (ft.) From	Depth (ft.) To
Black Dirt	0	1
Yellow Clay	1	15
Yellow Sand	15	19
Gray Clay	19	38
Gray Muddy sand	38	40
Gray Clay	40	70
Blue sand	70	76
Blue Clay	76	124
Rock	124	126
Blue Clay	126	139
Green Clay & sand	139	141
Blue Clay	141	152
Blue Sand	152	153
Blue Clay	153	198
Blue Gray Clay	198	203
Blue Gray sand	203	223

(Use separate sheet if necessary.)

10. DATE COMPLETED 6-7-77

11. WAS WELL PLUGGED OR ABANDONED?

☐ Yes ☒ No

If so, how

12. REMARKS:

13. DRILLER'S CERTIFICATION

This well was drilled under my jurisdiction and this report is true to the best of my knowledge.

James Brunner 31

Driller's or Firm's Name Certificate No.

Napoleon, N. Dak.

Address

James Brunner 6-7-77

Signed by Date

DUPLICATE — BOARD'S COPY
