STATE OF NORTH DAKOTA

BOARD OF WATER WELL CONTRACTORS

900 E. BOULEVARD • BISMARCK, NORTH DAKOTA 58501

WELL DRILLER'S REPORT

State law requires that this report be filed with the State Board of Water Well Contractors within 30 days after completion or abandonment of the well.

1. WELL OWNER

Name JIM BROUSSEAU

Address RR 1 Box 5 STEELE

2. WELL LOCATION

Sketch map location must agree with written location.

NORTH

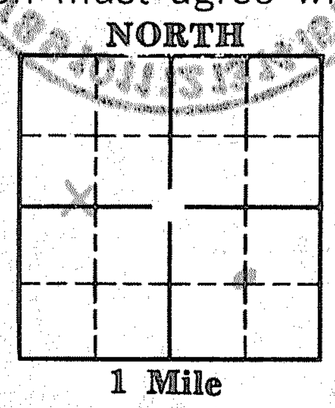

1 Mile

County Kidder

___ ¼ NW ¼ ___ ¼ Sec. 7 Twp. 140 N. Rg. 72 W.

3. PROPOSED USE

☐ Geothermal
☒ Domestic ☐ Irrigation ☐ Industrial
☐ Stock ☐ Municipal ☐ Test Hole

4. METHOD DRILLED

☐ Cable ☐ Reverse Rotary ☐ Bored
☒ Forward Rotary ☐ Jetted ☐ Other

If other, specify ___

5. WATER QUALITY

Was a water sample collected for chemical analysis?

☐ Yes ☒ No

If so, to what laboratory was it sent ___

6. WELL CONSTRUCTION

Diameter of hole 7 inches. Depth 140 feet.

Casing: ☐ Steel ☒ Plastic ☐ Concrete
☐ Threaded ☐ Welded ☐ Other

If other, specify ___

Pipe Weight:	Diameter:	From:	To:
___ lb/ft.	4 inches	1 feet	122 feet
___ lb/ft.	___ inches	___ feet	___ feet
___ lb/ft.	___ inches	___ feet	___ feet
___ lb/ft.	___ inches	___ feet	___ feet
___ lb/ft.	___ inches	___ feet	___ feet

Was perforated pipe used? ☒ Yes ☐ No

Length of pipe perforated 20 feet

Was casing left open end? ☐ Yes ☒ No

Was a well screened installed? ☐ Yes ☒ No

Material ___ Diameter ___ inches
(stainless steel, bronze, etc.)

Slot size ___ set from ___ feet to ___ feet

Slot size ___ set from ___ feet to ___ feet

Slot size ___ set from ___ feet to ___ feet

Slot size ___ set from ___ feet to ___ feet

Was a packer or seal used? ☐ Yes ☒ No

If so, what material ___

Type of well: Straight screen ☐ Gravel packed ☒

Was the well grouted? Yes ☒ No ☐

To what depth? 10 to 30 feet

Material used in grouting neat Cement

Well head completion: Pitless adapter ___

12" above grade X Other ___

If other, specify ___

Was well disinfected upon completion? ☒ Yes ☐ No

7. WATER LEVEL

Static water level 16 feet below land surface

If flowing: closed-in pressure ___ psi

GPM flow ___ through ___ inch pipe

Controlled by: ☐ Valve ☐ Reducers ☐ Other

If other, specify ___

8. WELL TEST DATA

☒ Pump ☐ Bailer ☐ Other

Pumping level below land surface:

30 ft. after 2½ hrs. pumping 11 gpm

___ ft. after ___ hrs. pumping ___ gpm

___ ft. after ___ hrs. pumping ___ gpm

9. WELL LOG

Formation	Depth (ft.) From	Depth (ft.) To
BLACK DIRT	0	1
LIGHT BROWN SAND	1	40
CLAY AND SAND	40	70
ROCK	70	72
GRAVEL AND SAND	72	90
SCHALE	90	92
BLUE SAND	92	122
BLACK SAND	122	140

(Use separate sheet if necessary.)

10. DATE COMPLETED 6-23-1995

11. WAS WELL PLUGGED OR ABANDONED?

☐ Yes ☒ No

If so, how ___

12. REMARKS: Jim Brousseau
will have water tested
Pitless unit will be installed

13. DRILLER'S CERTIFICATION

This well was drilled under my jurisdiction and this report is true to the best of my knowledge.

Witte Drilling 149
Driller's or Firm's Name Certificate No.

510 3rd N.W. Mandan N.D.
Address

Jasper Witte 6-23-1995
Signed by Date

WHITE—DRILLER'S COPY YELLOW—BOARD'S COPY PINK—CUSTOMER'S COPY
