STATE OF NORTH DAKOTA

BOARD OF WATER WELL CONTRACTORS

900 E. BOULEVARD • BISMARCK, NORTH DAKOTA 58501

WELL DRILLER'S REPORT

State law requires that this report be filed with the State Board of Water Well Contractors within 30 days after completion or abandonment of the well.

1. WELL OWNER

Name Marvin Schnabel

Address 5611 Hwy 3 Napoleon

2. WELL LOCATION

Sketch map location must agree with written location.

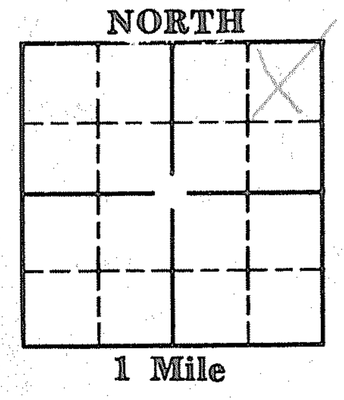

County Logan

NE ¼ ___ ¼ ___ ¼ Sec. 18 Twp. 136 N. Rg. 72 W.

3. PROPOSED USE

☐ Geothermal
☒ Domestic ☐ Irrigation ☐ Industrial
☐ Stock ☐ Municipal ☐ Test Hole

4. METHOD DRILLED

☐ Cable ☐ Reverse Rotary ☐ Bored
☒ Forward Rotary ☐ Jetted ☐ Other

If other, specify

5. WATER QUALITY

Was a water sample collected for chemical analysis?

☐ Yes ☒ No

If so, to what laboratory was it sent

6. WELL CONSTRUCTION

Diameter of hole 7 inches. Depth 200 feet.

Casing: ☐ Steel ☒ Plastic ☐ Concrete
☐ Threaded ☐ Welded ☐ Other

If other, specify

Pipe Weight:	Diameter:	From:	To:
lb/ft.	4 inches	2 feet	184 feet
lb/ft.	inches	feet	feet
lb/ft.	inches	feet	feet
lb/ft.	inches	feet	feet

Was perforated pipe used? ☒ Yes ☐ No

Length of pipe perforated 20 feet

Was casing left open end? ☐ Yes ☒ No

Was a well screened installed? ☐ Yes ☒ No

Material ___ Diameter ___ inches
(stainless steel, bronze, etc.)

Slot size ___ set from ___ feet to ___ feet

Slot size ___ set from ___ feet to ___ feet

Slot size ___ set from ___ feet to ___ feet

Slot size ___ set from ___ feet to ___ feet

Was a packer or seal used? ☐ Yes ☒ No

If so, what material

Type of well: Straight screen ☐ Gravel packed ☒

Was the well grouted? Yes ☒ No ☐

To what depth? 10 to 30 feet

Material used in grouting neat cement

Well head completion: Pitless adapter ___

12" above grade ___ Other ___

If other, specify

Was well disinfected upon completion? ☒ Yes ☐ No

7. WATER LEVEL

Static water level 40 feet below land surface

If flowing: closed in pressure ___ psi

GPM flow ___ through ___ inch pipe

Controlled by: ☐ Valve ☐ Reducers ☐ Other

If other, specify

8. WELL TEST DATA

☒ Pump ☐ Bailer ☐ Other

Pumping level below land surface:

90 ft. after 2 hr. 15 min hrs. pumping 10 gpm

___ ft. after ___ hrs. pumping ___ gpm

___ ft. after ___ hrs. pumping ___ gpm

9. WELL LOG

Formation	Depth (ft.) From	Depth (ft.) To
BLACK DIRT	0	1
GRAVEL AND ROCK	1	50
BLUE SAND	50	60
GRAY CLAY	60	150
BLUE SAND	150	184
CLAY	184	200

(Use separate sheet if necessary.)

10. DATE COMPLETED 8-5-1995

11. WAS WELL PLUGGED OR ABANDONED?

☐ Yes ☒ No

If so, how

12. REMARKS: well will have water tested pitless unit will be installed

Marvin Schnabel

13. DRILLER'S CERTIFICATION

This well was drilled under my jurisdiction and this report is true to the best of my knowledge.

Westbo Drilling 149

Driller's or Firm's Name Certificate No.

510 3rd ave N.W. Mandan ND

Address

Roger Westbo 8-6-95

Signed by Date

WHITE—DRILLER'S COPY YELLOW—BOARD'S COPY PINK—CUSTOMER'S COPY
