STATE OF NORTH DAKOTA

BOARD OF WATER WELL CONTRACTORS

900 E. BOULEVARD • BISMARCK, NORTH DAKOTA 58501

WELL DRILLER'S REPORT

State law requires that this report be filed with the State Board of Water Well Contractors within 30 days after completion or abandonment of the well.

1. WELL OWNER

Name Mr. Val Berhardt

Address Flasher, N. D.

2. WELL LOCATION

Sketch map location must agree with written location.

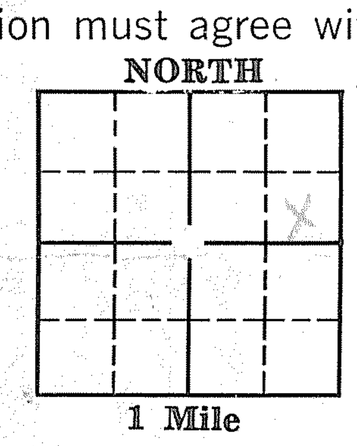

County Morton

NE ¼ ___ ¼ ___ ¼ Sec. 36 Twp. 135 N. Rg. 83 W.

3. PROPOSED USE

☐ Domestic ☐ Irrigation ☐ Industrial
☒ Stock ☐ Municipal ☐ Test Hole

4. METHOD DRILLED

☐ Cable ☐ Reverse Rotary ☐ Bored
☒ Forward Rotary ☐ Jetted ☐ Other

If other, specify

5. WATER QUALITY

Was a water sample collected for chemical analysis?

☐ Yes ☒ No

If so, to what laboratory was it sent

6. WELL CONSTRUCTION

Diameter of hole 6¼ inches. Depth 320 feet.

Casing: ☐ Steel ☒ Plastic ☐ Concrete
☐ Threaded ☐ Welded ☐ Other

If other, specify

Pipe Weight:	Diameter:	From:	To:
200 lb/ft.	4 inches	0 feet	320 feet
lb/ft.	inches	feet	feet
lb/ft.	inches	feet	feet
lb/ft.	inches	feet	feet

Was perforated pipe used? ☒ Yes ☐ No

Length of pipe perforated 20 feet

Was casing left open end? ☒ Yes ☐ No

Was a well screened installed? ☐ Yes ☒ No

Material ___ Diameter ___ inches
(stainless steel, bronze, etc.)

Slot size ___ set from ___ feet to ___ feet

Slot size ___ set from ___ feet to ___ feet

Slot size ___ set from ___ feet to ___ feet

Slot size ___ set from ___ feet to ___ feet

Was a packer or seal used? ☐ Yes ☒ No

If so, what material

Type of well: Straight screen ☐ Gravel packed ☒

Was the well grouted? Yes ☒ No ☐

To what depth? 8 feet

Material used in grouting neat cement

Well head completion: Pitless adapter

12" above grade X Other

If other, specify

Was well disinfected upon completion? ☒ Yes ☐ No

7. WATER LEVEL

Static water level 200 feet below land surface

If flowing: closed-in pressure ___ psi

GPM flow ___ through ___ inch pipe

Controlled by: ☐ Valve ☐ Reducers ☐ Other

If other, specify

8. WELL TEST DATA

☒ Pump ☒ Bailer ☐ Other

Pumping level below land surface:

220 ft. after 6 hrs. pumping 6 gpm

___ ft. after ___ hrs. pumping ___ gpm

___ ft. after ___ hrs. pumping ___ gpm

9. WELL LOG

Formation	Depth (ft.) From	Depth (ft.) To
Black dirt	0	4
white sand	4	25
yellow sand	25	42
clay	42	280
clay and sand	280	300
blue sand	300	320

(Use separate sheet if necessary.)

10. DATE COMPLETED June 3, 1977

11. WAS WELL PLUGGED OR ABANDONED?

☐ Yes ☒ No

If so, how

12. REMARKS:

13. DRILLER'S CERTIFICATION

This well was drilled under my jurisdiction and this report is true to the best of my knowledge.

Penced Water Systems 57

Driller's or Firm's Name Certificate No.

Glen Allen

Address

Penced Water Systems 6-3-77

Signed by Date

DUPLICATE — BOARD'S COPY
