STATE OF NORTH DAKOTA

BOARD OF WATER WELL CONTRACTORS

900 E. BOULEVARD • BISMARCK, NORTH DAKOTA 58501

WELL DRILLER'S REPORT

State law requires that this report be filed with the State Board of Water Well Contractors within 30 days after completion or abandonment of the well.

1. WELL OWNER

Name Norman Bling

Address Bottineau, ND

2. WELL LOCATION

Sketch map location must agree with written location.

NORTH

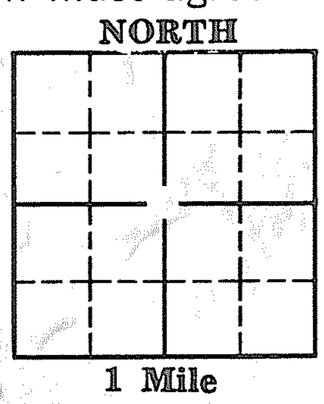

1 Mile

County Bottineau

____ ¼ ____ ¼ SE ¼ Sec. 26 Twp. 162 N. Rg. 76 W.

3. PROPOSED USE

☐ Domestic ☐ Irrigation ☐ Industrial
☐ Stock ☐ Municipal ☐ Test Hole

4. METHOD DRILLED

☐ Cable ☒ Reverse Rotary ☐ Bored
☐ Forward Rotary ☐ Jetted ☐ Other

If other, specify ____

5. WATER QUALITY

Was a water sample collected for chemical analysis?

☐ Yes ☒ No

If so, to what laboratory was it sent ____

6. WELL CONSTRUCTION

Diameter of hole 4 inches. Depth 80 feet.

Casing: ☐ Steel ☒ Plastic ☐ Concrete
☐ Threaded ☐ Welded ☐ Other

If other, specify glued

Pipe Weight:	Diameter:	From:	To:
20 lb/ft.	4 inches	0 feet	80 feet
____ lb/ft.	____ inches	____ feet	____ feet
____ lb/ft.	____ inches	____ feet	____ feet
____ lb/ft.	____ inches	____ feet	____ feet

Was perforated pipe used? ☐ Yes ☒ No

Length of pipe perforated ____ feet

Was casing left open end? ☐ Yes ☒ No

Was a well screened installed? ☒ Yes ☐ No

Material plastic Diameter 4 inches
(stainless steel, bronze, etc.)

Slot size 50 set from 60 feet to 80 feet

Slot size ____ set from ____ feet to ____ feet

Slot size ____ set from ____ feet to ____ feet

Was a packer or seal used? ☐ Yes ☒ No

If so, what material ____

Type of well: Straight screen ☐ Gravel packed ☒

Was the well grouted? Yes ☒ No ☐

To what depth? 20 ft feet

Material used in grouting cement

Well head completion: Pitless adapter ____

12" above grade ____ Other ____

If other, specify 16" above ground

Was well disinfected upon completion? ☒ Yes ☐ No

7. WATER LEVEL

Static water level 30 feet below land surface

If flowing: closed-in pressure ____ psi

GPM flow ____ through ____ inch pipe

Controlled by: ☐ Valve ☐ Reducers ☐ Other

If other, specify ____

8. WELL TEST DATA well makes about 2 gpm

☐ Pump ☐ Bailer ☐ Other

Pumping level below land surface:

____ ft. after ____ hrs. pumping ____ gpm

____ ft. after ____ hrs. pumping ____ gpm

____ ft. after ____ hrs. pumping ____ gpm

9. WELL LOG

Formation	Depth (ft.) From	Depth (ft.) To
surface	0	1
yellow clay	1	18
blue clay	18	35
gravel (dry)	35	43
blue clay	43	59
gray muddy sand some water	59	78
clay	78	80

(Use separate sheet if necessary.)

10. DATE COMPLETED November 6, 1987

11. WAS WELL PLUGGED OR ABANDONED?

☐ Yes ☒ No

If so, how ____

12. REMARKS: well is located north of Lange

13. DRILLER'S CERTIFICATION

This well was drilled under my jurisdiction and this report is true to the best of my knowledge.

Mariner Drilling Service 38

Driller's or Firm's Name Certificate No.

Box 57 Minot, ND

Address

Kenny Jarvis 12-2-87

Signed by Date

WHITE—DRILLER'S COPY YELLOW—BOARD'S COPY PINK—CUSTOMER'S COPY
