STATE OF NORTH DAKOTA

# BOARD OF WATER WELL CONTRACTORS

900 E. BOULEVARD • BISMARCK, NORTH DAKOTA 58501

# WELL DRILLER'S REPORT

State law requires that this report be filed with the State Board of Water Well Contractors within 30 days after completion or abandonment of the well.

**1. WELL OWNER**

Name M & J. Equipment Co. Inc

Address Bottineau, N. Dak.

**2. WELL LOCATION**

Sketch map location must agree with written location.

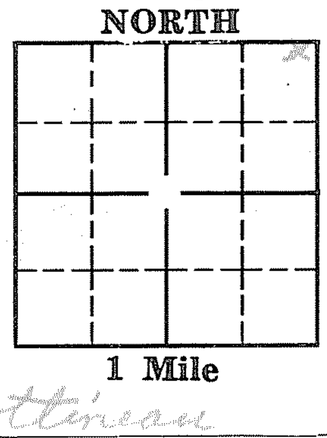


County Bottineau

NE ¼ NE ¼ NE ¼ Sec. 35 Twp. 162 N. Rg. 76 W.

**3. PROPOSED USE**

☒ Domestic ☐ Irrigation ☐ Industrial
☐ Stock ☐ Municipal ☐ Test Hole

**4. METHOD DRILLED**

☐ Cable ☐ Reverse Rotary ☒ Bored
☐ Forward Rotary ☐ Jetted ☐ Other

If other, specify

**5. WATER QUALITY**

Was a water sample collected for chemical analysis?

☐ Yes ☒ No

If so, to what laboratory was it sent

**6. WELL CONSTRUCTION**

Diameter of hole 36 inches. Depth 30 feet.

Casing: ☒ Steel ☐ Plastic ☐ Concrete
☐ Threaded ☐ Welded ☐ Other

If other, specify

| Pipe Weight: | Diameter: | From: | To: |
|---|---|---|---|
| lb/ft. | 36 inches | 0 feet | 12 feet |
| lb/ft. | 24 inches | 12 feet | 30 feet |
| lb/ft. | inches | feet | feet |
| lb/ft. | inches | feet | feet |

Was perforated pipe used? ☒ Yes ☐ No

Length of pipe perforated feet

Was casing left open end? ☒ Yes ☐ No

Was a well screened installed? ☐ Yes ☒ No

Material Diameter inches
(stainless steel, bronze, etc.)

Slot size set from feet to feet

Slot size set from feet to feet

Slot size set from feet to feet

Was a packer or seal used? ☐ Yes ☒ No

If so, what material

Type of well: Straight screen ☐ Gravel packed ☐

Was the well grouted? Yes ☐ No ☐

To what depth? feet

Material used in grouting Concrete

Well head completion: Pitless adapter

12" above grade Other

If other, specify

Was well disinfected upon completion? ☐ Yes ☒ No

**7. WATER LEVEL**

Static water level 7' feet below land surface

If flowing: closed-in pressure psi

GPM flow through inch pipe

Controlled by: ☐ Valve ☐ Reducers ☐ Other

If other, specify

**8. WELL TEST DATA**

☐ Pump ☐ Bailer ☐ Other

Pumping level below land surface:

ft. after hrs. pumping gpm

ft. after hrs. pumping gpm

ft. after hrs. pumping gpm

**9. WELL LOG**

| Formation | Depth (ft.) From | Depth (ft.) To |
|---|---|---|
| Top soil | 0 | 3' |
| yellow clay | 3' | 5' |
| Sand | 5' | 12' |
| CLAY | 12 | 14' |
| Sand | 14 | 30' |

(Use separate sheet if necessary.)

**10. DATE COMPLETED** May 22 1975

**11. WAS WELL PLUGGED OR ABANDONED?**

☐ Yes ☒ No

If so, how

**12. REMARKS:**

Dug down with 36" casing to 12 ft then went inside w/ 24" pipe to 30 ft

**13. DRILLER'S CERTIFICATION**

This well was drilled under my jurisdiction and this report is true to the best of my knowledge.

Vinco Well Drilling 100

Driller's or Firm's Name Certificate No.

Bottineau N. Dak

Address

Vinco Dahlberg May 22-75

Signed by Date

DUPLICATE — BOARD'S COPY
