STATE OF NORTH DAKOTA

BOARD OF WATER WELL CONTRACTORS

900 E. BOULEVARD • BISMARCK, NORTH DAKOTA 58501

WELL DRILLER'S REPORT

State law requires that this report be filed with the State Board of Water Well Contractors within 30 days after completion or abandonment of the well.

1. WELL OWNER

Name Richard Johnson

Address Rolla, N.D.

2. WELL LOCATION

Sketch map location must agree with written location.

NORTH

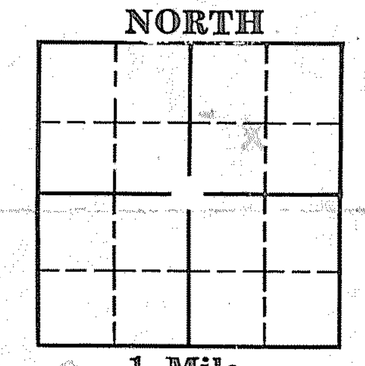

1 Mile

County Rolette

NE ¼ SW ¼ NE ¼ Sec. 36 Twp. 163 N. Rg. 87 W.

3. PROPOSED USE

☐ Domestic ☐ Irrigation ☐ Industrial

☒ Stock ☐ Municipal ☐ Test Hole

4. METHOD DRILLED

☐ Cable ☐ Reverse Rotary ☒ Bored

☐ Forward Rotary ☐ Jetted ☐ Other

If other, specify

5. WATER QUALITY

Was a water sample collected for chemical analysis?

☐ Yes ☒ No

If so, to what laboratory was it sent

6. WELL CONSTRUCTION

Diameter of hole 24" inches. Depth 30' feet.

Casing: ☐ Steel ☐ Plastic ☒ Concrete

☐ Threaded ☐ Welded ☐ Other

If other, specify None

Pipe Weight:	Diameter:	From:	To:
lb/ft.	24" inches	0 feet	30' feet
lb/ft.	inches	feet	feet
lb/ft.	inches	feet	feet
lb/ft.	inches	feet	feet

Was perforated pipe used? ☒ Yes ☐ No

Length of pipe perforated 8 ft. feet

Was casing left open end? ☒ Yes ☐ No

Was a well screened installed? ☒ Yes ☐ No

Material Concrete Diameter 24" inches
(stainless steel, bronze, etc.)

Slot size None set from feet to feet

Slot size set from feet to feet

Slot size set from feet to feet

Slot size set from feet to feet

Was a packer or seal used? ☐ Yes ☒ No

If so, what material None

Type of well: Straight screen ☐ Gravel packed ☒

Was the well grouted? Yes ☒ No ☐

To what depth? 10' feet

Material used in grouting Clay

Well head completion: Pitless adapter None

12" above grade None Other None

If other, specify None

Was well disinfected upon completion? ☐ Yes ☒ No

7. WATER LEVEL

Static water level 14' feet below land surface

If flowing: closed-in pressure None psi

GPM flow None through inch pipe

Controlled by: ☐ Valve ☐ Reducers ☐ Other

If other, specify None

8. WELL TEST DATA

☐ Pump ☐ Bailer ☐ Other

Pumping level below land surface:

None ft. after hrs. pumping gpm

ft. after hrs. pumping gpm

ft. after hrs. pumping gpm

9. WELL LOG

Formation	Depth (ft.) From	Depth (ft.) To
Clay	0	14'
Sand	14'	16'
Sandy Clay	16'	30'

(Use separate sheet if necessary.)

10. DATE COMPLETED Nov. 15, 1979

11. WAS WELL PLUGGED OR ABANDONED?

☐ Yes ☒ No

If so, how

12. REMARKS:

13. DRILLER'S CERTIFICATION

This well was drilled under my jurisdiction and this report is true to the best of my knowledge.

Carter Water Well Drilling 145

Driller's or Firm's Name Certificate No.

Sherwood, N.D.

Address

Ross Carter Nov. 23/79

Signed by Date

DUPLICATE — BOARD'S COPY
