STATE OF NORTH DAKOTA

BOARD OF WATER WELL CONTRACTORS

900 E. BOULEVARD • BISMARCK, NORTH DAKOTA 58501

WELL DRILLER'S REPORT

State law requires that this report be filed with the State Board of Water Well Contractors within 30 days after completion or abandonment of the well.

1. WELL OWNER

Name Robert Hanson

Address Sherwood

2. WELL LOCATION

Sketch map location must agree with written location.

NORTH

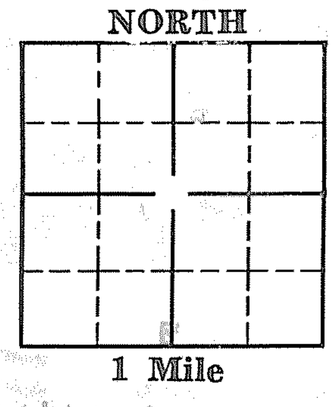

1 Mile

County Renville

SE ¼ SE ¼ SW ¼ Sec. 22 Twp. 164 N. Rg. 86 W.

3. PROPOSED USE

☑ Domestic ☐ Irrigation ☐ Industrial

☐ Stock ☐ Municipal ☐ Test Hole

4. METHOD DRILLED

☐ Cable ☐ Reverse Rotary ☑ Bored

☐ Forward Rotary ☐ Jetted ☐ Other

If other, specify

5. WATER QUALITY

Was a water sample collected for chemical analysis?

☐ Yes ☐ No

If so, to what laboratory was it sent

6. WELL CONSTRUCTION

Diameter of hole 24 inches. Depth 45 feet.

Casing: ☐ Steel ☐ Plastic ☐ Concrete

☐ Threaded ☐ Welded ☐ Other

If other, specify Dug

Pipe Weight:	Diameter:	From:	To:
lb/ft.	inches	feet	feet
lb/ft.	inches	feet	feet
lb/ft.	inches	feet	feet
lb/ft.	inches	feet	feet

Was perforated pipe used? ☐ Yes ☐ No

Length of pipe perforated None feet

Was casing left open end? ☐ Yes ☐ No

Was a well screened installed? ☐ Yes ☐ No

Material (stainless steel, bronze, etc.) Diameter inches

Slot size set from feet to feet

Slot size set from feet to feet

Slot size set from feet to feet

Slot size set from feet to feet

Was a packer or seal used? ☐ Yes ☐ No

If so, what material

Type of well: Straight screen ☐ Gravel packed ☐

Was the well grouted? Yes ☐ No ☐

To what depth? None feet

Material used in grouting

Well head completion: Pitless adapter

12" above grade Other

If other, specify

Was well disinfected upon completion? ☐ Yes ☐ No

7. WATER LEVEL

Static water level feet below land surface

If flowing: closed-in pressure psi

GPM flow through inch pipe

Controlled by: ☐ Valve ☐ Reducers ☐ Other

If other, specify

8. WELL TEST DATA

☐ Pump ☐ Bailer ☐ Other

Pumping level below land surface:

ft. after hrs. pumping gpm

ft. after hrs. pumping gpm

ft. after hrs. pumping gpm

9. WELL LOG

Formation	Depth (ft.) From	Depth (ft.) To
top soil	0	1
yellow clay	1	20
blue clay & Rocks	20	45

(Use separate sheet if necessary.)

10. DATE COMPLETED 11-13-74

11. WAS WELL PLUGGED OR ABANDONED?

☐ Yes ☐ No

If so, how Back filled

12. REMARKS:

13. DRILLER'S CERTIFICATION

This well was drilled under my jurisdiction and this report is true to the best of my knowledge.

Virgil Well Drilling 100

Driller's or Firm's Name Certificate No.

Bottineau N. Dak. 58318

Address

Virgil Dahlberg 11-14-74

Signed by Date

DUPLICATE — BOARD'S COPY
