STATE OF NORTH DAKOTA

BOARD OF WATER WELL CONTRACTORS

900 E. BOULEVARD • BISMARCK, NORTH DAKOTA 58501

WELL DRILLER'S REPORT

State law requires that this report be filed with the State Board of Water Well Contractors within 30 days after completion or abandonment of the well.

1. WELL OWNER

Name Watford City Rediman

Address Watford City, N.D.

2. WELL LOCATION

Sketch map location must agree with written location.

NORTH

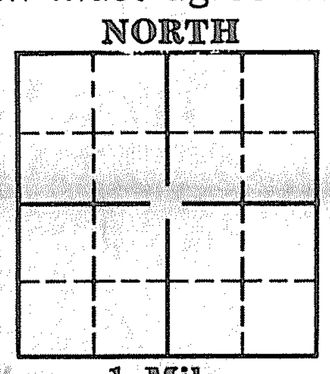

1 Mile

County Mountrail

NW ¼ NW ¼ NW ¼ Sec. 21 Twp. 152 N. Rg. 92 W.

3. PROPOSED USE

☐ Domestic ☐ Irrigation ☒ Industrial
☐ Stock ☐ Municipal ☐ Test Hole

4. METHOD DRILLED

☐ Cable ☐ Reverse Rotary ☐ Bored
☒ Forward Rotary ☐ Jetted ☐ Other

If other, specify

5. WATER QUALITY

Was a water sample collected for chemical analysis?

☐ Yes ☒ No

If so, to what laboratory was it sent

6. WELL CONSTRUCTION

Diameter of hole 7⅞ inches. Depth 210 feet.

Casing: ☐ Steel ☒ Plastic ☐ Concrete
☐ Threaded ☐ Welded ☐ Other

If other, specify

Pipe Weight:	Diameter:	From:	To:
200 lb/ft.	4 inches	+1 feet	210 feet
lb/ft.	inches	feet	feet
lb/ft.	inches	feet	feet
lb/ft.	inches	feet	feet

Was perforated pipe used? ☒ Yes ☐ No

Length of pipe perforated 30 feet

Was casing left open end? ☐ Yes ☒ No

Was a well screened installed? ☐ Yes ☒ No

Material _____ Diameter _____ inches
(stainless steel, bronze, etc.)

Slot size _____ set from _____ feet to _____ feet

Slot size _____ set from _____ feet to _____ feet

Slot size _____ set from _____ feet to _____ feet

Slot size _____ set from _____ feet to _____ feet

Was a packer or seal used? ☐ Yes ☒ No

If so, what material

Type of well: Straight screen ☐ Gravel packed ☒

Was the well grouted? Yes ☒ No ☐

To what depth? 80 feet

Material used in grouting Cement

Well head completion: Pitless adapter

12" above grade X Other

If other, specify

Was well disinfected upon completion? ☒ Yes ☐ No

7. WATER LEVEL

Static water level 80 feet below land surface

If flowing: closed-in pressure _____ psi

GPM flow _____ through _____ inch pipe

Controlled by: ☐ Valve ☐ Reducers ☐ Other

If other, specify

8. WELL TEST DATA

☒ Pump ☐ Bailer ☐ Other

Pumping level below land surface:

160 ft. after 2 hrs. pumping 7 gpm

_____ ft. after _____ hrs. pumping _____ gpm

_____ ft. after _____ hrs. pumping _____ gpm

9. WELL LOG

Formation	Depth (ft.) From	Depth (ft.) To
topsoil	0	1
sand	1	7
gravel	8	18
sand & clay layers	18	52
clay	52	140
clay & stone	140	185
sandy clay mud	185	195
muddy sand	195	210

(Use separate sheet if necessary.)

10. DATE COMPLETED May 85

11. WAS WELL PLUGGED OR ABANDONED?

☐ Yes ☒ No

If so, how

12. REMARKS:

13. DRILLER'S CERTIFICATION

This well was drilled under my jurisdiction and this report is true to the best of my knowledge.

SAX WELL DRILLING — 47
Driller's or Firm's Name — Certificate No.

Watford City, N.D.
Address

[signature] — May 85
Signed by — Date

WHITE—DRILLER'S COPY YELLOW—BOARD'S COPY PINK—CUSTOMER'S COPY
