STATE OF NORTH DAKOTA

BOARD OF WATER WELL CONTRACTORS

900 E. BOULEVARD AVE., DEPT. 770 • BISMARCK, NORTH DAKOTA 58505-0850

WELL DRILLER'S REPORT

State law requires that this report be filed with the State Board of Water Well Contractors within 30 days after completion or abandonment of the well.

1. WELL OWNER

Name: Scott Nelson

Address: 110 Valley St., Lisbon, ND 58054

2. WELL LOCATION

Sketch map location must agree with written location.

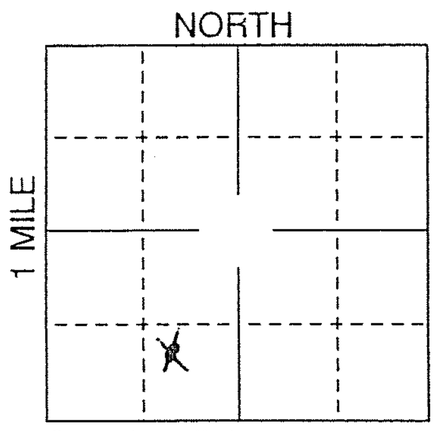

Sec. (1 mile) _____

County: Ransom

NE 1/4 SE 1/4 SW 1/4 Sec. 29 Twp. 134 N. Rg. 54 W.

3. PROPOSED USE

☒ Domestic ☐ Stock ☐ Geothermal ☐ Irrigation ☐ Municipal ☐ Monitoring ☐ Industrial ☐ Test Hole

4. METHOD DRILLED

☐ Cable ☐ Reverse Rotary ☐ Bored

☒ Forward Rotary ☐ Jetted ☐ Auger

If other, specify _____

5. WATER QUALITY

Was a water sample collected for:

Chemical Analysis? ☐ Yes ☒ No

Bacteriological Analysis? ☐ Yes ☒ No

If so, to what laboratory was it sent? _____

6. WELL CONSTRUCTION

Diameter of hole 8 1/2 inches. Depth 50 feet.

Casing: ☐ Steel ☒ Plastic ☐ Concrete ☐ Threaded ☐ Welded ☐ Other

If other, specify _____

Pipe Weight:	Diameter:	From:	To:
200 lb/ft	5 inches	0 feet	40 feet
lb/ft	inches	feet	feet
lb/ft	inches	feet	feet

Was perforated pipe used? ☐ Yes ☒ No

Perforated pipe set from _____ ft. to _____ feet

Was casing left open end? ☐ Yes ☒ No

Was a well screen installed? ☒ Yes ☐ No

Material PVC Diameter 5 inches

Slot Size 020 set from 40 feet to 50 feet

Slot Size _____ set from _____ feet to _____ feet

Was packer or seal used? ☐ Yes ☒ No

If so, what material _____ Depth _____ ft.

Type of well: Straight screen ☐ Gravel packed ☒

Depth grouted: From 6 To 35

Grouting Material: Cement _____ Other X

If other, explain: Wyo-Ben one step bentonite 6 Bags

Well head completion: Pitless unit yes

12" above grade X Other _____

If other, specify _____

Was pump installed? ☒ Yes ☐ No

Was well disinfected upon completion? ☒ Yes ☐ No

7. WATER LEVEL

Static water level 12 feet below surface

If flowing: closed-in pressure _____ psi

GPM flow _____ through _____ inch pipe

Controlled by: ☐ Valve ☐ Reducers ☐ Other

If other, specify _____

8. WELL TEST DATA

☐ Pump ☐ Bailer ☒ Other AIR

Pumping level below land surface:

20 ft. after 1 hrs. pumping 20 gpm

_____ ft. after _____ hrs. pumping _____ gpm

_____ ft. after _____ hrs. pumping _____ gpm

9. WELL LOG

Formation	Depth (ft.) From	Depth (ft.) To
Black top soil	0	2
yellow clay	2	15
Blue clay	15	30
Blue clay hard	30	40
water sand gray	40	50

(Use separate sheet if necessary)

10. DATE COMPLETED 12/1/09

11. WAS WELL PLUGGED OR ABANDONED?

☐ Yes ☒ No

If so, how _____

12. REMARKS:

13. DRILLER'S CERTIFICATION

This well was drilled under my jurisdiction and this report is true to the best of my knowledge.

Wieber Well — Driller's or Firm's Name

190 — Certificate No.

157, Ledgerwood, ND 58053 — Address

Jerry Wieber — Signed by

12/1/09 — Date
