STATE OF NORTH DAKOTA

BOARD OF WATER WELL CONTRACTORS

900 E. BOULEVARD • BISMARCK, NORTH DAKOTA 58501

WELL DRILLER'S REPORT

State law requires that this report be filed with the State Board of Water Well Contractors within 30 days after completion or abandonment of the well.

1. WELL OWNER

Name: Ken Doppler

Address: RR#1 Box 82 Menoken

2. WELL LOCATION

Sketch map location must agree with written location.

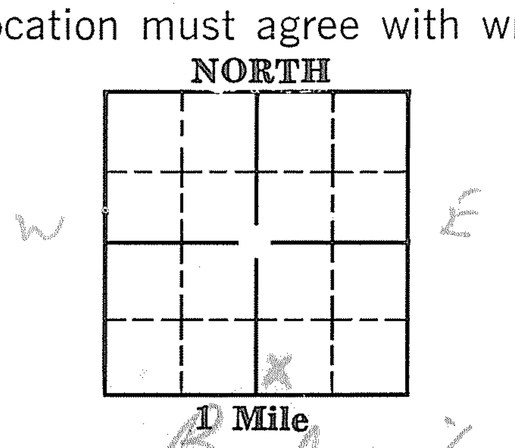

County: Burleigh

SW ¼ SW ¼ SE ¼ Sec. 29 Twp. 138 N. Rg. 78 W.

3. PROPOSED USE

☒ Domestic ☐ Irrigation ☐ Industrial
☐ Stock ☐ Municipal ☐ Test Hole

4. METHOD DRILLED

☐ Cable ☐ Reverse Rotary ☐ Bored
☒ Forward Rotary ☐ Jetted ☐ Other

If other, specify

5. WATER QUALITY

Was a water sample collected for chemical analysis?

☐ Yes ☒ No

If so, to what laboratory was it sent

6. WELL CONSTRUCTION

Diameter of hole 6 3/4 inches. Depth 160 feet.

Casing: ☐ Steel ☐ Plastic ☐ Concrete
☐ Threaded ☐ Welded ☐ Other

If other, specify

Pipe Weight:	Diameter:	From:	To:
200 lb/ft.	4 inches	0 feet	160 feet
lb/ft.	inches	feet	feet
lb/ft.	inches	feet	feet
lb/ft.	inches	feet	feet

Was perforated pipe used? ☒ Yes ☐ No

Length of pipe perforated 30 feet

Was casing left open end? ☐ Yes ☒ No

Was a well screened installed? ☐ Yes ☐ No

Material _____ Diameter _____ inches
(stainless steel, bronze, etc.)

Slot size _____ set from _____ feet to _____ feet

Slot size _____ set from _____ feet to _____ feet

Slot size _____ set from _____ feet to _____ feet

Slot size _____ set from _____ feet to _____ feet

Was a packer or seal used? ☐ Yes ☐ No

If so, what material

Type of well: Straight screen ☐ Gravel packed ☒ sand

Was the well grouted? Yes ☒ No ☐

To what depth? 60 back filled with clay feet

Material used in grouting

Well head completion: Pitless adapter X

12" above grade _____ Other _____

If other, specify

Was well disinfected upon completion? ☒ Yes ☐ No

7. WATER LEVEL

Static water level 65 feet below land surface

If flowing: closed-in pressure _____ psi

GPM flow _____ through _____ inch pipe

Controlled by: ☐ Valve ☐ Reducers ☐ Other

If other, specify

8. WELL TEST DATA

☒ Pump ☐ Bailer ☐ Other

Pumping level below land surface:

67 ft. after 1 hrs. pumping 12 gpm

_____ ft. after _____ hrs. pumping _____ gpm

_____ ft. after _____ hrs. pumping _____ gpm

9. WELL LOG

Formation	Depth (ft.) From	Depth (ft.) To
surface soil	0	1
soft clay & silt	1	30
coal	30	31
gra clay & silt	31	150
rock	150	152
green sand	152	160

(Use separate sheet if necessary.)

10. DATE COMPLETED Sept 3-82

11. WAS WELL PLUGGED OR ABANDONED?

☐ Yes ☒ No

If so, how

12. REMARKS: new location in field

13. DRILLER'S CERTIFICATION

This well was drilled under my jurisdiction and this report is true to the best of my knowledge.

Weld Drilling — 35
Driller's or Firm's Name — Certificate No.

Box 472
Address

Mandan, N.D.

Signed by Neb Weld — Date Sept 20 82
